

HOSPIRA INFORMATION TECHNOLOGY STANDARD OPERATING PROCEDURE

Document Number ITSOP-137	Title Resource Management Process		
Supersedes N/A	Issue Date 05/08/2007	Effective On or Before 05/11/2007	Page 1 of 8

Approvals

Role	Name	Date Approved
Originator	Timothy K. Julian	05/07/2007
First Five + Program Manager	Katrina Burmeister	05/08/2007
Manager, IT Compliance Management	Leslie Wood	05/08/2007

TABLE OF CONTENTS

Section	Page
1.0 PURPOSE.....	2
2.0 SCOPE	2
3.0 REFERENCES.....	2
4.0 DEFINITIONS	2
5.0 RESPONSIBILITIES	3
6.0 PROCESS.....	4
6.1 RESOURCE REQUEST PROCESSING (RM 1.0).....	4
6.1.1 Receive Resource Request (RM 1.1).....	5
6.1.5 Assign Resource(s) (RM 1.5).....	6
6.1.6 Resource Re-alignment Impact Assessment (RM 1.6).....	6
6.1.7 Resource Re-assignment (RM 1.7).....	6
6.2 RESOURCE TRACKING (RM 2.0)	7
6.2.1 Analyze Potential Upcoming Projects (RM 2.1).....	8
6.2.2 Resource Status Monitoring (RM 2.2)	8
6.2.3 Update Resource Repository (RM 2.3).....	8
7.0 ATTACHMENTS	8
8.0 REASON FOR CHANGE	8

HOSPIRA INFORMATION TECHNOLOGY STANDARD OPERATING PROCEDURE

Document Number ITSOP-137	Title Resource Management Process		
Supersedes N/A	Issue Date 05/08/2007	Effective On or Before 05/11/2007	Page 2 of 8

1.0 PURPOSE

This document describes the process for resource request processing and resource tracking used in the IT Resource Management process.

2.0 SCOPE

The scope of the Resource Management Process described in this document includes ad hoc Tier 2 and Tier 3 project requests.

3.0 REFERENCES

Identifier	Title
ITSOP-139	Demand Management Process

4.0 DEFINITIONS

Term	Definition
eProject©	Application-Service-Provider-hosted project management tool used to manage IT demand and resources.
Resource Manager	IT Managers or Team Leads who assign resources to projects/tasks in eProject©.
Tier 1	Projects less than a specified dollar threshold , meets technical criteria and support resources are available
Tier 2	Projects greater than a dollar threshold, meets technical criteria, development resources available, and business has funding
Tier 3	Projects greater than a dollar threshold, meets technical criteria, development resources available, and cross functional impact

HOSPIRA INFORMATION TECHNOLOGY STANDARD OPERATING PROCEDURE

Document Number ITSOP-137	Title Resource Management Process		
Supersedes N/A	Issue Date 05/08/2007	Effective On or Before 05/11/2007	Page 3 of 8

5.0 RESPONSIBILITIES


Role	Responsibility
Relationship Manager	Request resource/PM for project
Resource Supply Coordinator / Resource Manager	Assign, re-assign or decline resources and hours to requests.
Hospira Information Technology	Implementing this procedure
IT Compliance Management	Administers the maintenance of this procedure

HOSPIRA INFORMATION TECHNOLOGY STANDARD OPERATING PROCEDURE

Document Number ITSOP-137	Title Resource Management Process		
Supersedes N/A	Issue Date 05/08/2007	Effective On or Before 05/11/2007	Page 4 of 8

6.0 PROCESS

6.1 RESOURCE REQUEST PROCESSING (RM 1.0)

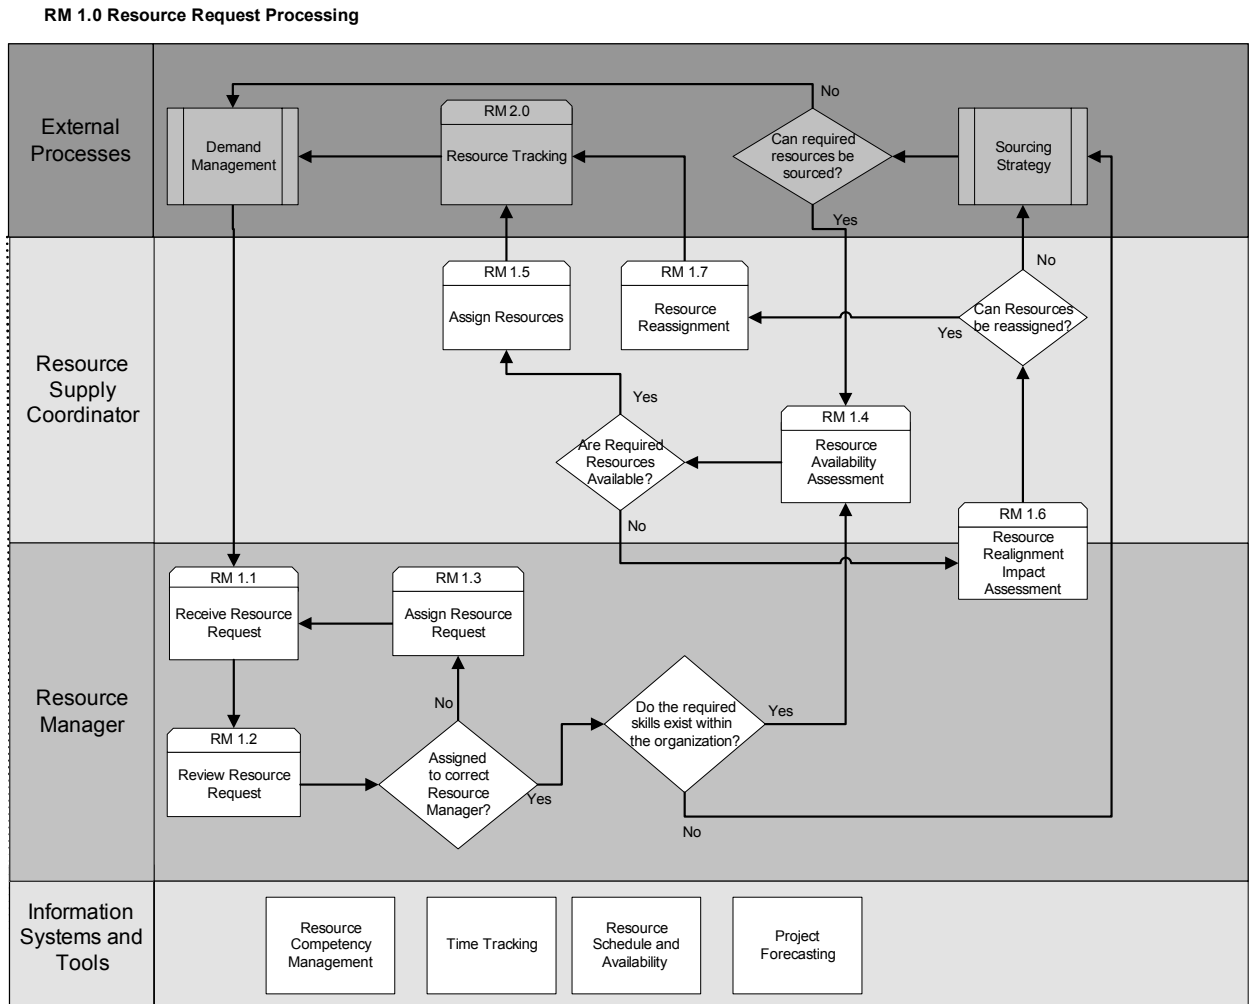

Resource Request Processing will be followed by all Resource Managers to approve or decline resource requests for IT work (demand). Specific named resources will be assigned to specific projects or other demand such as Incidents (break/fix) or other requests. For the sake of the current implementation of this process, the "Resource Supply Coordinator" and the "Resource Manager" are one and the same. These are the actual managers of the resources themselves or, on larger teams, Team Leads may fulfill this role.

HOSPIRA INFORMATION TECHNOLOGY STANDARD OPERATING PROCEDURE

Document Number ITSOP-137	Title Resource Management Process		
Supersedes N/A	Issue Date 05/08/2007	Effective On or Before 05/11/2007	Page 5 of 8

Resource Managers should project out as far as they can for known project work and at least 2 months out for non-project work (incidents, requests, etc). This process should be followed minimally every 2 weeks by the Resource Managers.

6.1.1 Receive Resource Request (RM 1.1)

The Resource Manager will receive resource requests for projects from the Demand Management Process. The Demand Process requires the project to be entered into eProject©. The Relationship Manager and/or the IT RC assigns the Resource Manager to the project as an eProject© "Project Manager". This generates an email request for the Resource Manager that states: "The following Project has been generated from a Project request and you have been assigned as the Project Manager."

Review Resource Request (RM 1.2)

eProject© is the tool that will be used to manage and monitor resource requests. Please note that Tier 1 requests (see Demand Management process) will be assigned/monitored in Service Desk. To review the resource request, access eProject©. Several methods can be used to review the resource request:

- a. Click on the email received and that will take you to eProject©, click on the Resources Menu on the left. Then click on the Resource Allocation tab. This will display which Resource Types and hours per month or week were requested for this project. At a minimum, 1 Resource Type must have been entered by the Relationship Manager/IT RC.
- b. Select the Team Manager tab and any Projects requesting resources will display under the 'Pending Resource Requests' section. At a minimum, 1 Resource Type must have been entered by the Relationship Manager/IT RC.

The requests should be reviewed to determine if the project resource request is correctly assigned to your area. If it is and the resource(s) with skills required exists, proceed to step 6.1.4. If it is not a resource in your area, proceed to step 6.1.3.

Note: At this time 'skills' are a general type such as Project Manager, Data Base Administrator, etc.

6.1.3 Re-assign Resource Request (RM 1.3)

If the request was not for a resource in your area, decline the request in eProject©. This routes the email back to the requestor so that they can re-route to the correct Resource Manager.

6.1.4 Resource Availability Assessment (RM 1.4)

The Resource Manager reviews the availability of the Resource Type requested using eProject©. This is done by viewing the Team Manager tab in eProject© that reflects

HOSPIRA INFORMATION TECHNOLOGY STANDARD OPERATING PROCEDURE

Document Number ITSOP-137	Title Resource Management Process		
Supersedes N/A	Issue Date 05/08/2007	Effective On or Before 05/11/2007	Page 6 of 8

Pending Resource Requests and the Hours Requested vs. Assigned and also Resource Assignments and the Hours Available vs. Assigned for all the resources and projects for their area. Due to the fact that eProject© does not display the demand score in the Team Manager view, it is necessary to review the report that displays all demand with corresponding scores to determine the prioritization of the resource requests.

6.1.5 Assign Resource(s) (RM 1.5)

Assign the resource to the request. This is done in eProject© from the Team Manager tab by clicking on the Actions button next to the Resource Type requested for the project and selecting 'Assign Resources'. The full hours requested can be assigned to one resource or split up among more resources and can be entered weekly or monthly.

Note: The view can be changed from Weekly to Monthly or visa versa in the upper left of the screen. Once the resources and hours are entered, select 'Approval All Resources' from the Actions button. An email will be sent back to the Requestor.

Resources should be assigned to the highest priority demand first, moving down the list to lower priority demand until no more resources are available to be assigned. If no more resources are available, the Resource Manager should decline the resource request due to insufficient resources.

6.1.6 Resource Re-alignment Impact Assessment (RM 1.6)

The Resource Manager reviews assignments and makes adjustments to resource assignments based on staffing workload, project issues or changes, etc. It may be possible to reallocate resources in order to fulfill a resource request which may not initially be possible to fulfill due to lack of resources. This step of the process allows the Resource Manager to reconsider their current resource assignments to open up the possibility to realign their resources to fulfill the request.


6.1.7 Resource Re-assignment (RM 1.7)

If resources need to be re-assigned, re-assign the resources in eProject©. Select the project and resource type to be re-allocated using the Actions button under the Resource Assignments section of the Team Manager tab. This moves the request back under the Pending tab to be re-assigned.

HOSPIRA INFORMATION TECHNOLOGY STANDARD OPERATING PROCEDURE

Document Number ITSOP-137	Title Resource Management Process		
Supersedes N/A	Issue Date 05/08/2007	Effective On or Before 05/11/2007	Page 7 of 8

6.2 RESOURCE TRACKING (RM 2.0)

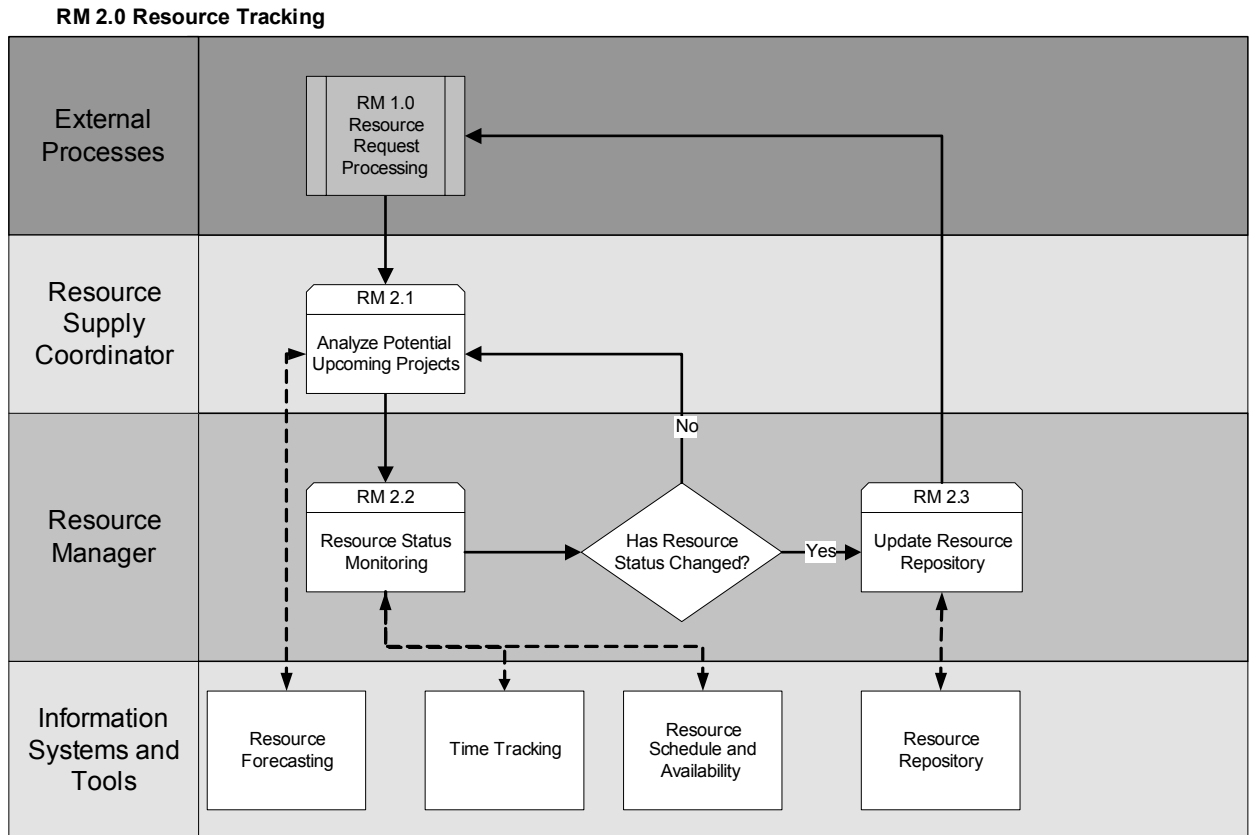

The Resource Tracking process is the process that will be followed by all Resource Managers to monitor their resources and demand. As resources change this process allows for adjusting the resource repository accordingly. As Resource Managers become aware of distant projects that may require additional resources, they can plan for that accordingly and get necessary resources on board to accommodate that future demand.

For the sake of the current implementation of this process, the “Resource Supply Coordinator” and the “Resource Manager” are one and the same. These are the actual managers of the resources themselves or, on larger teams, Team Leads may fulfill this role.

This process should be followed minimally every 2 weeks by the Resource Managers in conjunction with the Resource Request Processing.

HOSPIRA INFORMATION TECHNOLOGY STANDARD OPERATING PROCEDURE

Document Number ITSOP-137	Title Resource Management Process		
Supersedes N/A	Issue Date 05/08/2007	Effective On or Before 05/11/2007	Page 8 of 8

6.2.1 Analyze Potential Upcoming Projects (RM 2.1)

The Resource Manager will analyze upcoming demand. This can be from formal resource requests following the Resource Request Process, or could be adjustments for increased support needs due to project rollouts or other things the Resource Manager may become aware of.

6.2.2 Resource Status Monitoring (RM 2.2)

The Resource Manager will consistently monitor their resources and adjust the resource repository as necessary. Resources may change due to new hires, retirements, leaves of absence, vacations, role changes, skill changes, etc.

6.2.3 Update Resource Repository (RM 2.3)

If changes are necessary due to Resource Status Monitoring, the Resource Manager will update their resources in the resource repository (eProject©) accordingly.

7.0 ATTACHMENTS

None

8.0 REASON FOR CHANGE

Description of change

Section	Change Description/Purpose
New document	New Document
